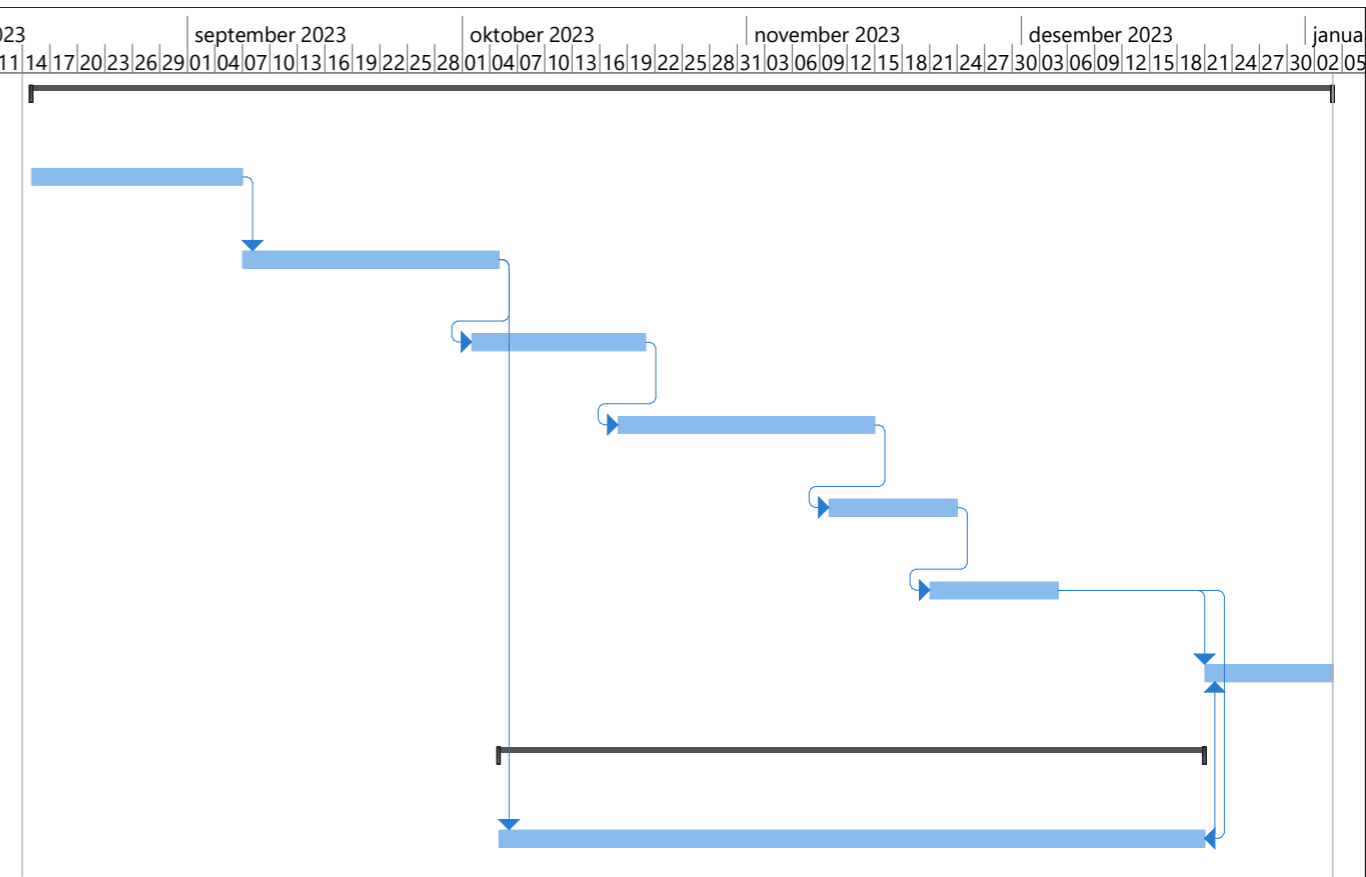




















ID	Aktivitetstype	Aktivitetsnavn	Varighet	Start	Slutt	Foregående aktiviteter	Navn på ressurser	2023	september 2023	oktober 2023	november 2023	desember 2023	januar
								08 11 14 17 20 23 26 29 01 04 07 10 13 16 19 22 25 28 31	01 04 07 10 13 16 19 22 25 28 31	01 04 07 10 13 16 19 22 25 28 31	03 06 09 12 15 18 21 24 27 30	03 06 09 12 15 18 21 24 27 30	01 02 03 04 05
1		<b>DEL 1 - Takarbeider</b>	<b>102 dager</b>	<b>ti 15.08.23</b>	<b>on 03.01.24</b>								
2		Tilrigging og tak over tak	17 dager	ti 15.08.23	on 06.09.23								
3		Rivearbeider	20 dager	to 07.09.23	on 04.10.23	2							
4		Stålarbeider	15 dager	ma 02.10.23	fr 20.10.23	3AS-3 dager							
5		Tømrerarbeid	20 dager	on 18.10.23	ti 14.11.23	4AS-3 dager							
6		Taktekking	10 dager	fr 10.11.23	to 23.11.23	5AS-3 dager							
7		Blikkenslager	10 dager	ti 21.11.23	ma 04.12.23	6AS-3 dager							
8		Nedrigg tak over tak	10 dager	to 21.12.23	on 03.01.24	7;10							
9		<b>DEL 2 - Solcelleanlegg</b>	<b>55 dager</b>	<b>to 05.10.23</b>	<b>on 20.12.23</b>								
10		Montasje solceller	55 dager	to 05.10.23	on 20.12.23	3;7AA+10 dager							



Prosjekt: Fremdriftsplan Dato: ma 26.06.23	Aktivitet		Inaktiv aktivitet		Manuell sammendragsfremheving		Ekstern milepæl	
	Deling		Inaktiv milepæl		Manuelt sammendrag		Tidsfrist	
	Milepæl		Inaktivt sammendrag		Bare start		Fremdrift	
	Sammendrag		Manuell aktivitet		Bare slutt		Manuell fremdrift	
	Prosjektsammendrag		Bare varighet		Eksterne aktiviteter			

Prosjekt: Fremdriftsplan  
 Dato: ma 26.06.23

Aktivitet		Inaktiv aktivitet		Manuell sammendrag fremheving		Ekstern milepæl	
Deling		Inaktiv milepæl		Manuelt sammendrag		Tidsfrist	
Milepæl		Inaktivt sammendrag		Bare start		Fremdrift	
Sammendrag		Manuell aktivitet		Bare slutt		Manuell fremdrift	
Prosjektsammendrag		Bare varighet		Eksterne aktiviteter	
